


# Excelsior Restoration Update

9-24-2021

- Building #5 – All of the punch list items are completed. The Excelsior staff has started the cleaning process and repainting of parking lines in the garage. Still looking for a window washer.
- Villas – Still waiting on an opportunity to repair the 5 columns. Not urgent as the worker's focus is on the gulf building given the amount of work to be done.

- Gulf Building – Material removal on the walkways within the first two columns of section one are done and the concrete pours are completed. The support posts must remain in place for 14 days for full concrete cure.
- Work continues on the stairs and lanais.
- All the tile on the lanais of the first five floors (X01 Tower) have been removed due to evidence of water pooling under the tile and causing concrete damage. We are looking for replacement coatings for both the lanais and walkways as they will need to be coated very soon after the repairs to provide proper waterproofing.

# Gulf Building Photos Restoration

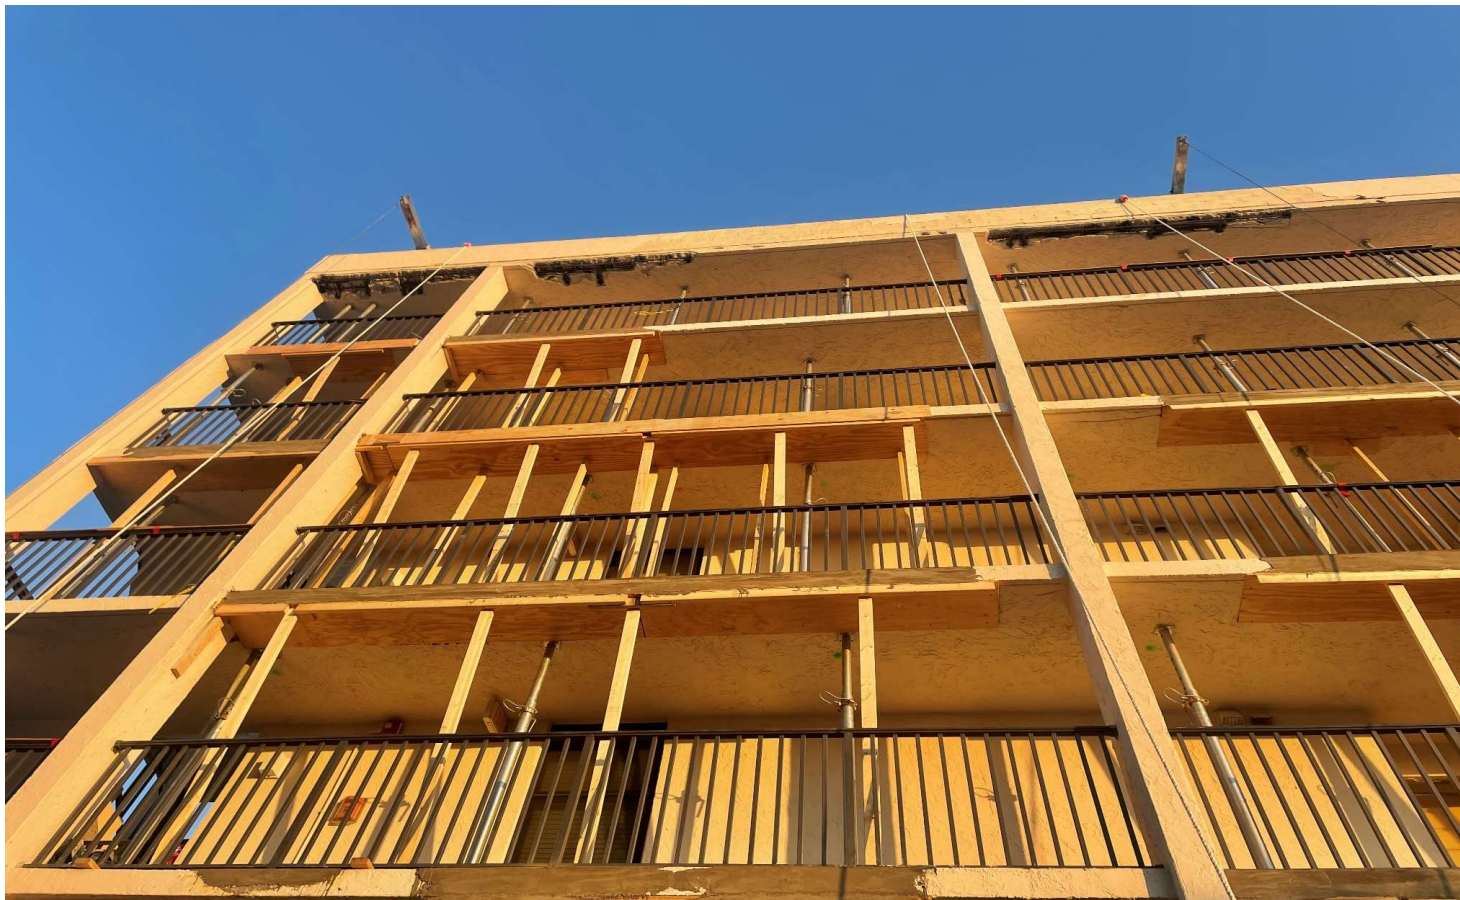

# Gulf Building Photos Restoration

